



ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration	
1	1.1	ILCTA control			1%	779 days?	
2	1.1.1	ILCTA control design			13%	341 days?	
3	1.1.1.1	Prototype - A0 Photo Injector			33%	322 days	
4	1.1.1.1.1	Develop prototype A0 3.9 Ghz			44%	200 days	
5	1.1.1.1.2	OTR Server	Piccoli_FNAL		0%	1 day	
6	1.1.1.1.2.1	Package and put in fnkits			0%	1 day	
7	1.1.1.1.3	Deploy Double Dogleg Beamline			0%	1 day	
8	1.1.1.1.3.1	Stepping motor control, 3 new motors			0%	1 day?	
9	1.1.1.1.3.2	Actuators, 3 new devices, chassis mods			0%	1 day?	
10	1.1.1.1.3.3	Magnet power supplies with interface displays			0%	1 day?	
11	1.1.1.1.3.4	Interface to vacuums			0%	1 day?	
12	1.1.1.1.3.5	Clock system interface			0%	1 day?	
13	1.1.1.1.3.6	Wooster upgrade			0%	1 day?	
14	1.1.1.1.4	Integrate prototype 3.9 GHz photoinjector			0%	1 day	
15	1.1.1.1.4.1	Integrate hardware			0%	1 day	
16	1.1.1.1.4.2	Integrate DOOCS			0%	1 day	
17	1.1.1.1.4.3	Integration and demonstration of control system			0%	1 day	
18	1.1.1.1.5	Integrate A0 1.3GHz Photoinjector		28SF-5 days	0%	20 days	
19	1.1.1.1.6	Design integrated A0 control system			0%	1 day	
20	1.1.1.1.6.1	Sequencer			0%	1 day?	
21	1.1.1.1.6.2	Archiving			0%	1 day	
22	1.1.1.1.6.3	Alarming			0%	1 day	




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
23	1.1.1.1.6.4	Save/restore			0%	1 day
24	1.1.1.1.6.5	Data retrieval/analysis			0%	1 day
25	1.1.1.1.6.6	Configuration management			0%	1 day
26	1.1.1.1.6.7	A0 Controls Design Document complete			0%	1 day
27	1.1.1.1.7	A0 experiment begins			0%	1 day
28	1.1.1.1.8	Integrate 1.3 GHz photoinjector		29SF-10 days	0%	20 days
29	1.1.1.1.9	Move A0 1.3 & 3.9 GHz Photoinjector to NML		252SF-10 days	0%	10 days
30	1.1.1.2	Design HTS control for Meson Lab			0%	150 days
31	1.1.1.2.1	Document HTS control requirements and system specificatio	Marsh_FNAL		0%	1 day
32	1.1.1.2.2	Design HTS control system hardware	Kucera_FNAL		0%	150 days
33	1.1.1.2.3	Design HTS control software system			0%	1 day
34	1.1.1.2.3.1	Design Remote Operations from MCR			0%	1 day
35	1.1.1.3	Design - NML control			0%	254 days?
36	1.1.1.3.1	Define NML system requirements	Krause_FNAL		0%	100 days
37	1.1.1.3.1.1	Evaluate NML control prototype			0%	100 days
38	1.1.1.3.1.2	Document NML control system requirements			0%	1 day
39	1.1.1.3.2	Design hardware architecture			0%	254 days?
40	1.1.1.3.2.1	Define hardware layout			0%	1 day
41	1.1.1.3.2.2	Evaluate NML hardware options			0%	1 day
42	1.1.1.3.2.2.1	HITECH			0%	1 day
43	1.1.1.3.2.2.2	CosyLab			0%	1 day
44	1.1.1.3.2.2.3	DAQ harware			0%	1 day




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
45	1.1.1.3.2.3	Controls computing			2%	43 days?
46	1.1.1.3.2.3.1	Deploy control room			3%	33 days?
47	1.1.1.3.2.3.1.1	Network switch installation for control room			0%	5 days
48	1.1.1.3.2.3.1.2	Networking			0%	1 day?
49	1.1.1.3.2.3.1.3	Servers			0%	1 day
50	1.1.1.3.2.3.1.4	Console systems			30%	1 day
51	1.1.1.3.2.3.1.5	Procure controls electronics			0%	1 day
52	1.1.1.3.2.3.1.6	Mobile console			0%	1 day
53	1.1.1.3.2.3.1.7	Deploy UPS			0%	1 day
54	1.1.1.3.2.3.2	NML Control room ready		46	0%	10 days
55	1.1.1.3.2.4	Deploy Instrumentation interface			0%	1 day
56	1.1.1.3.2.5	Deploy LLRF interface			0%	1 day
57	1.1.1.3.2.6	Deploy Safety system interface			0%	1 day
58	1.1.1.3.2.7	Design and deploy timing system - slow timing	Kucera_FNAL		0%	30 days
59	1.1.1.3.2.8	Deploy interfaces to phase referencing (w/LLRF)			0%	1 day
60	1.1.1.3.2.9	Design Timestamping standard			0%	1 day
61	1.1.1.3.2.10	Document cable specification for interconnecting contro			0%	40 days
62	1.1.1.3.2.11	Document hardware architecture			0%	40 days
63	1.1.1.3.3	Design software architecture			0%	1 day
64	1.1.1.3.3.1	Design to combine DOOCS, EPICS, Labview, MatLab			0%	1 day
65	1.1.1.3.3.2	Archiving design			0%	1 day
66	1.1.1.3.3.3	Alarm design			0%	1 day




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
67	1.1.1.3.3.4	DAQ design			0%	1 day
68	1.1.1.3.3.5	Diagnostic tools			0%	1 day
69	1.1.1.3.3.6	Design EPICS enabled hardware			0%	1 day
70	1.1.1.3.3.7	Define display system strategy			0%	1 day
71	1.1.1.3.3.8	Document software architecture			0%	1 day
72	1.1.1.3.4	Design NML control system HW/SW interfaces			0%	1 day?
73	1.1.1.3.4.1	Interface to instrumentation			0%	1 day
74	1.1.1.3.4.2	Interface to HLRF			0%	1 day
75	1.1.1.3.4.3	Interface to LLRF			0%	1 day
76	1.1.1.3.4.4	Interface to Machine Protection System			0%	1 day
77	1.1.1.3.4.5	Interface to Human safety system			0%	1 day
78	1.1.1.3.4.6	Interface to Cryo system			0%	1 day
79	1.1.1.3.4.7	Interface to Piezo Tuner	4Ruben_FNAL		0%	1 day
80	1.1.1.3.4.8	Interface to slow tuner control for cavities			0%	1 day?
81	1.1.1.3.4.9	Interface to the coupler actuator control			0%	1 day?
82	1.1.1.3.4.10	Interface of EPICS to PLCs			0%	1 day
83	1.1.1.3.5	Procure and establish NML test stand			0%	1 day
84	1.1.2	ILCTA control implementation			2%	238 days?
85	1.1.2.1	Integrate system - VTS control			0%	1 day
86	1.1.2.1.1	Network installations & IP/MAC setup			0%	1 day
87	1.1.2.1.2	Implement software			0%	1 day
88	1.1.2.1.2.1	Deploy Jlab Labview system	4Ruben_FNAL		0%	1 day




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
89	1.1.2.1.2.2	Interface to cryo cavity data management software	4Ruben_FNAL		0%	1 day
90	1.1.2.1.2.3	Interface to electronic logbook	4Ruben_FNAL		0%	1 day
91	1.1.2.1.3	Integrate firmware			0%	1 day
92	1.1.2.1.4	Integrate VTS control			0%	1 day
93	1.1.2.2	Integrate system - HTS control			0%	2 days
94	1.1.2.2.1	Integarte HTS hardware			0%	1 day
95	1.1.2.2.1.1	Network installations & IP/MAC setup			0%	1 day
96	1.1.2.2.2	Implement software			0%	2 days
97	1.1.2.2.2.1	Implement EPICS/DOOCS components			0%	2 days
98	1.1.2.2.2.1.1	Implement DOOCS/EPICS interface			0%	1 day
99	1.1.2.2.2.1.2	Deploy "standard" version of archiver	Firbaugh_FNAL		0%	1 day
100	1.1.2.2.2.1.3	Deploy/configure DOOCS2EPICS for archiving	Firbaugh_FNAL	99	0%	1 day
101	1.1.2.2.2.1.4	Deploy alarming			0%	1 day
102	1.1.2.2.2.1.5	Deploy DOOCS/EPICS interface to integrate LLRF	Nicklaus_FNAL	83	0%	1 day
103	1.1.2.2.2.1.6	Remove ACNET console			0%	1 day
104	1.1.2.2.2.1.7	Implement datalog devices			0%	1 day
105	1.1.2.2.2.1.8	Configure archiver with appropriate devices	Nicklaus_FNAL		0%	1 day
106	1.1.2.2.2.1.9	Replace SPARC Board with Linux	Rechenmacher_FNAL		0%	1 day
107	1.1.2.2.2.1.10	<i>Deploy cryogenics logging facility to EPICS?</i>	Sirotenko_FNAL		0%	1 day
108	1.1.2.2.2.2	Deploy HTS specific software feature			0%	1 day
109	1.1.2.2.2.2.1	Display additional channels (IRM)			0%	1 day?
110	1.1.2.2.2.2.2	Additional archiving			0%	1 day?




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
111	1.1.2.2.2.3	Alarming			0%	1 day?
112	1.1.2.2.3	Implement interface to cryo cavity data management soft			0%	1 day
113	1.1.2.2.4	Implement Coupler Conditioning Sequencer	Nicklaus_FNAL		0%	1 day
114	1.1.2.2.5	Implement control of slow tuner through EPICS	Nicklaus_FNAL		0%	1 day
115	1.1.2.2.6	Implement PC interface to network analyzer			0%	1 day
116	1.1.2.2.7	Implement calibrated Waveform displays	Nicklaus_FNAL		0%	1 day
117	1.1.2.2.8	Implement parameter pages	Nicklaus_FNAL		0%	1 day
118	1.1.2.2.9	Automation of various tasks	.FNAL,Nicklaus_FNAL		0%	1 day
119	1.1.2.2.10	Configure vacuum and temperatures into PLC (when H)	.FNAL,Nicklaus_FNAL		0%	1 day
120	1.1.2.2.11	Data retrieval/analysis	.FNAL,Nicklaus_FNAL		0%	1 day
121	1.1.2.2.12	Implement Remote Operations from MCR	.FNAL,Nicklaus_FNAL		0%	1 day
122	1.1.2.2.13	Version and tag PLC IOC	.FNAL,Nicklaus_FNAL		0%	1 day
123	1.1.2.2.14	Upgrade DOOCS server for new LLRF firmware	.FNAL,Nicklaus_FNAL		0%	1 day
124	1.1.2.2.15	Deploy Irmis	.FNAL,Nicklaus_FNAL		0%	1 day
125	1.1.2.3	Integrate and test firmware			0%	1 day
126	1.1.2.4	Integrate HTS control			0%	1 day
127	1.1.2.3	Integrate A0 hardware (at A0)	Kucera_FNAL		6%	195 days?
128	1.1.2.3.1	Prepare A0 hardware			0%	10 days
129	1.1.2.3.1.1	LLRF hardware (processor + ESECON)			0%	10 days
130	1.1.2.3.1.2	Existing controls crate (9)/modules testing			0%	10 days




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
131	1.1.2.3.1.3	Modify Timing module w/new trigger			0%	10 days
132	1.1.2.3.2	Complete Wooster replacement		128	0%	1 day
133	1.1.2.3.3	Spitefire 2 & 6 replacement?	Rechenmacher_FNAL		0%	1 day
134	1.1.2.3.4	Machine protection HW			100%	1 day
135	1.1.2.3.5	Human protection HW			100%	1 day
136	1.1.2.3.6	Install network connection for Wooster upgrade			0%	1 day?
137	1.1.2.4	Implement A0 specific software			0%	2 days
138	1.1.2.4.1	Replace Wooster with ESECON	Rechenmacher_FNAL	156	0%	1 day
139	1.1.2.4.2	Understand doocs responsive issues			0%	1 day
140	1.1.2.4.3	Update DDD displays to reflect current configuration			0%	1 day
141	1.1.2.4.4	Convert phasescan to GPIB over ethernet (to eliminate MA)	Davidsaver_FNAL		0%	1 day
142	1.1.2.4.5	Make DOOCS degauss server to elimate MAC	Davidsaver_FNAL		0%	1 day
143	1.1.2.5	Implement software NML			0%	238 days
144	1.1.2.5.1	Integrate A0 SW at NML			0%	1 day
145	1.1.2.5.2	Integrate NML software			0%	1 day
146	1.1.2.5.2.1	Event clock			0%	1 day?
147	1.1.2.5.2.2	Interface to safety rad monitors			0%	1 day?
148	1.1.2.5.2.3	CM1 motor control			0%	1 day?
149	1.1.2.5.2.4	CM2 RF interlock			0%	1 day?
150	1.1.2.5.2.5	Interface to safety critical devices			0%	1 day
151	1.1.2.5.2.6	Cryo control - rapid recovery from power outage			0%	1 day?
152	1.1.2.5.3	Install UPS			0%	1 day?




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
153	1.1.2.5.4	Make OTR server robust	Piccoli_FNAL		0%	1 day
154	1.1.2.5.5	BPM server mods (alarming, scaling)	Davidsaver_FNAL		0%	1 day
155	1.1.2.5.6	Multiknob support for magnet control	Piccoli_FNAL		0%	1 day
156	1.1.2.5.7	Obtain Linux X86 signoff from AD/LLRF			0%	1 day
157	1.1.2.5.8	Migrate Matlab code to DOOCS - Linux x86			0%	1 day?
158	1.1.2.5.9	Resolve MATLAB 2006 stability issue - OS upgrade	Rechenmacher_FNAL	229	0%	1 day
159	1.1.2.5.10	Deploy integrated controls systems in design doc	Davidsaver_FNAL		0%	1 day
160	1.1.2.5.11	Implement application software layer (need more details, jav			0%	1 day
161	1.1.2.5.12	Interface to cryo cavity data management software			0%	1 day
162	1.1.2.6	Implement Photocathode system			0%	1 day
163	1.1.2.6.1	Implement Photocathode Prep system			0%	1 day
164	1.1.2.6.2	Archiving			0%	1 day?
165	1.1.2.6.3	Prep chamber control			0%	1 day?
166	1.1.2.6.4	Transfer chamber control			0%	1 day?
167	1.1.2.7	Integrate system - NML			0%	1 day
168	1.1.2.7.1	Network installations & IP/MAC setup			0%	1 day
169	1.1.2.7.2	Implemanet firmware			0%	1 day
170	1.1.2.7.3	Move CC2 to NML			0%	1 day
171	1.1.2.7.4	Integrate NML			0%	1 day
172	1.1.3	Commissioning control system			0%	1 day
173	1.1.3.1	Commission VTS control			0%	1 day
174	1.1.3.2	Commission HTS control			0%	1 day




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
175	1.1.3.3	Commission NML control			0%	1 day
176	1.1.4	ILCTA control at NML operational		258SF-2 days	0%	1 day
177	1.1.5	ILCTA control software infrastructure			0%	478 days?
178	1.1.5.1	ILCTA control software configuration management			0%	1 day
179	1.1.5.1.1	Code organization			0%	1 day
180	1.1.5.1.1.1	Document EPICS code organization			0%	1 day
181	1.1.5.1.1.2	Document DOOCS code organization			0%	1 day
182	1.1.5.1.2	Build management			0%	1 day
183	1.1.5.1.2.1	Retool EPICS build system			0%	1 day
184	1.1.5.1.2.2	Stable integrated core software build process ready			0%	1 day
185	1.1.5.1.3	Release management			0%	1 day
186	1.1.5.1.3.1	EPICS release management			0%	1 day
187	1.1.5.1.3.2	DOOCS release management			0%	1 day
188	1.1.5.1.4	Interface management			0%	1 day
189	1.1.5.1.4.1	Develop DOOCS/EPICS interface from DESY			0%	1 day
190	1.1.5.1.4.2	EPICS/Doocs interface management infrastructure reac			0%	1 day
191	1.1.5.1.4.3	Document EPICs/DOOCS/Labview/Matlab/PLC interfac			0%	1 day
192	1.1.5.2	ILCTA controls software environment			0%	1 day
193	1.1.5.2.1	Maintain stable EPICS base environment			0%	1 day
194	1.1.5.2.1.1	Package the archiver in a distributable form			0%	1 day
195	1.1.5.2.1.2	Wirte Archiving Strategy Document			0%	1 day
196	1.1.5.2.1.3	Package/document IRMIS			0%	1 day




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
197	1.1.5.2.2	Maintain stable DOOCS environment			0%	1 day
198	1.1.5.2.2.1	Convert makefiles to gmake (from SunOS)			0%	1 day
199	1.1.5.2.2.2	Feedback makefiles to DESY			0%	1 day
200	1.1.5.2.2.3	Determine DOOCS/EPICS architecture automatically			0%	1 day
201	1.1.5.2.2.4	Remove hardcoded locations for MATLAB, etc			0%	1 day
202	1.1.5.2.2.5	Document & code LD_LIBRARY_PATH expansion			0%	1 day
203	1.1.5.2.3	Maintain hardware compatibility			0%	1 day
204	1.1.5.2.3.1	Evaluate ATCA			0%	1 day
205	1.1.5.2.3.2	Evaluate timing module			0%	1 day
206	1.1.5.2.4	Automate install/uninstall for Controls systems software			0%	1 day
207	1.1.5.2.5	Prepare for additional subnet			0%	1 day
208	1.1.5.2.6	Assure cross-training of personnel in the DOOCS and			0%	1 day?
209	1.1.5.2.7	Document ILCTA Controls Software Environment			0%	1 day
210	1.1.5.3	ILCTA system administration			0%	478 days?
211	1.1.5.3.1	System Support			0%	478 days
212	1.1.5.3.1.1	Document tracking & versioning for admin areas	Rechenmacher_FNAL		0%	1 day
213	1.1.5.3.1.2	Evaluate source code management tools (GIT)	Rechenmacher_FNAL		0%	30 days
214	1.1.5.3.1.3	Switchover to new source code management tool	Rechenmacher_FNAL	213	0%	1 day
215	1.1.5.3.1.4	Develop website ITCTA.FNAL.GOV	Votava_FNAL		0%	1 day
216	1.1.5.3.1.5	Backups	Sieh_FNAL		0%	478 days
217	1.1.5.3.1.6	Move A0 machines behind firewall	Rechenmacher_FNAL		0%	1 day
218	1.1.5.3.2	Product Support			0%	81 days




ILCTAControls_FNAL.mpp

ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
219	1.1.5.3.2.1	Develop workgroup for ILCTA	Sieh_FNAL		0%	10 days
220	1.1.5.3.2.2	Configure VNC servers on all ILCTA machines	Sieh_FNAL	219,229	0%	1 day
221	1.1.5.3.2.3	Setup webservers on selected ILCTA machines		219	0%	1 day
222	1.1.5.3.2.4	Order/install Matlab floating license			0%	1 day
223	1.1.5.3.2.5	Order/install LabView floating license			0%	1 day
224	1.1.5.3.2.6	Define & create a operator desktop environment			0%	60 days
225	1.1.5.3.3	Kernel Support			0%	199 days?
226	1.1.5.3.3.1	Create trace kernal RPM			0%	1 day
227	1.1.5.3.3.2	Firewire installed on all machines	Sieh_FNAL	229	0%	1 day
228	1.1.5.3.3.3	Complete evaluation LTS5	Rechenmacher_FNAL	230,219	0%	1 day?
229	1.1.5.3.3.4	Upgrade all machines to LTS5	Sieh_FNAL	228	0%	1 day
230	1.1.5.3.3.5	Document firewall settings	Rechenmacher_FNAL	221	0%	1 day
231	1.1.5.3.4	NML Computing Infrastructure			0%	297 days
232	1.1.5.3.4.1	Develop & document server plan			0%	10 days
233	1.1.5.3.4.2	Order computers and monitors FY07	Kucera_FNAL	232	0%	30 days
234	1.1.5.3.4.3	Order computers and monitors FY08	Kucera_FNAL		0%	30 days
235	1.1.5.3.4.4	SW install/configure computers/monitors	Sieh_FNAL	236,219,212	0%	5 days
236	1.1.5.3.4.5	HW install/configure computers/monitors		233	0%	5 days
237	1.1.6	ILCTA control technical management			0%	760 days
238	1.1.6.1	ILCTA control requirements management			0%	760 days
239	1.1.6.2	ILCTA control project management			0%	760 days
240	1.1.6.3	Support project webpage, wiki & document servers			0%	760 days




ILCTAControls_FNAL.mpp


ID	WBS	Task Name	Resource Names	Predecessors	% Complete	Duration
241	1.1.7	ILCTA control equipment purchases			0%	760 days
242	1.1.7.1	FY07 Hardware purchases			0%	760 days
243	1.1.7.2	FY08 Hardware purchases			0%	760 days
244	1.1.7.3	Misc software purchases			0%	760 days
245	1.2	NML Major Milestones (Jerry Leibfritz)			0%	469 days
246	1.2.1	Refrigerator #1 Operational			0%	0 days
247	1.2.2	Building Infrastructure Complete			0%	0 days
248	1.2.3	RF Systems Operational 5MW & CC2			0%	0 days
249	1.2.4	CCI2 Operational			0%	0 days
250	1.2.5	1st Cryomodule Delivery to NML			0%	0 days
251	1.2.6	Begin 1st Cryomodule RF Test Warm			0%	0 days
252	1.2.7	Begin Move of A0 Injector to NML			0%	0 days
253	1.2.8	Cryo System Components in Place			0%	0 days
254	1.2.9	Begin Cooldown of 1st Cryomodule			0%	0 days
255	1.2.10	Refrigerator #2 Operational			0%	0 days
256	1.2.11	2nd Cryomodule Delivery to NML			0%	0 days
257	1.2.12	Begin Civil Design of Build. Extension			0%	0 days
258	1.2.13	First Beam			0%	0 days
259	1.2.14	Order Cryoplant			0%	0 days
260	1.2.15	3rd Cryomodule Delivery to NML			0%	0 days



ILCTACControls_FNAL.mpp



ILCTAControls_FNAL.mpp

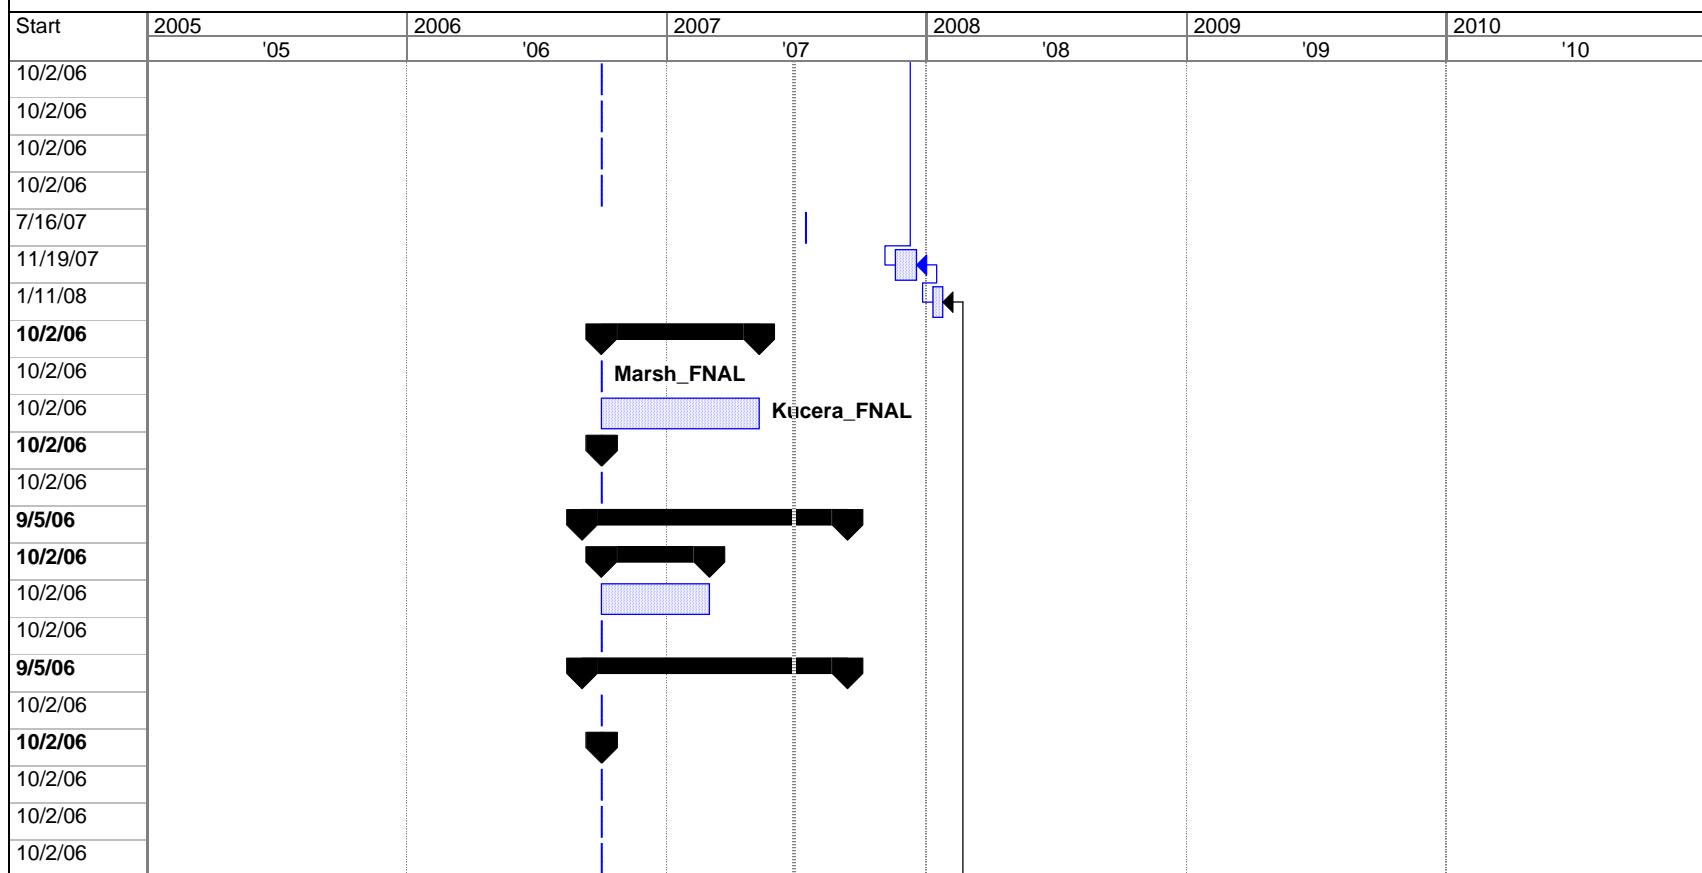

Project: ILCTAControls_FNAL.mpp
Date: 6/28/07

Task
Split
Progress



Milestone



External Tasks



Summary



External Milestone





Project Summary




Deadline




ILCTAControls_FNAL.mpp

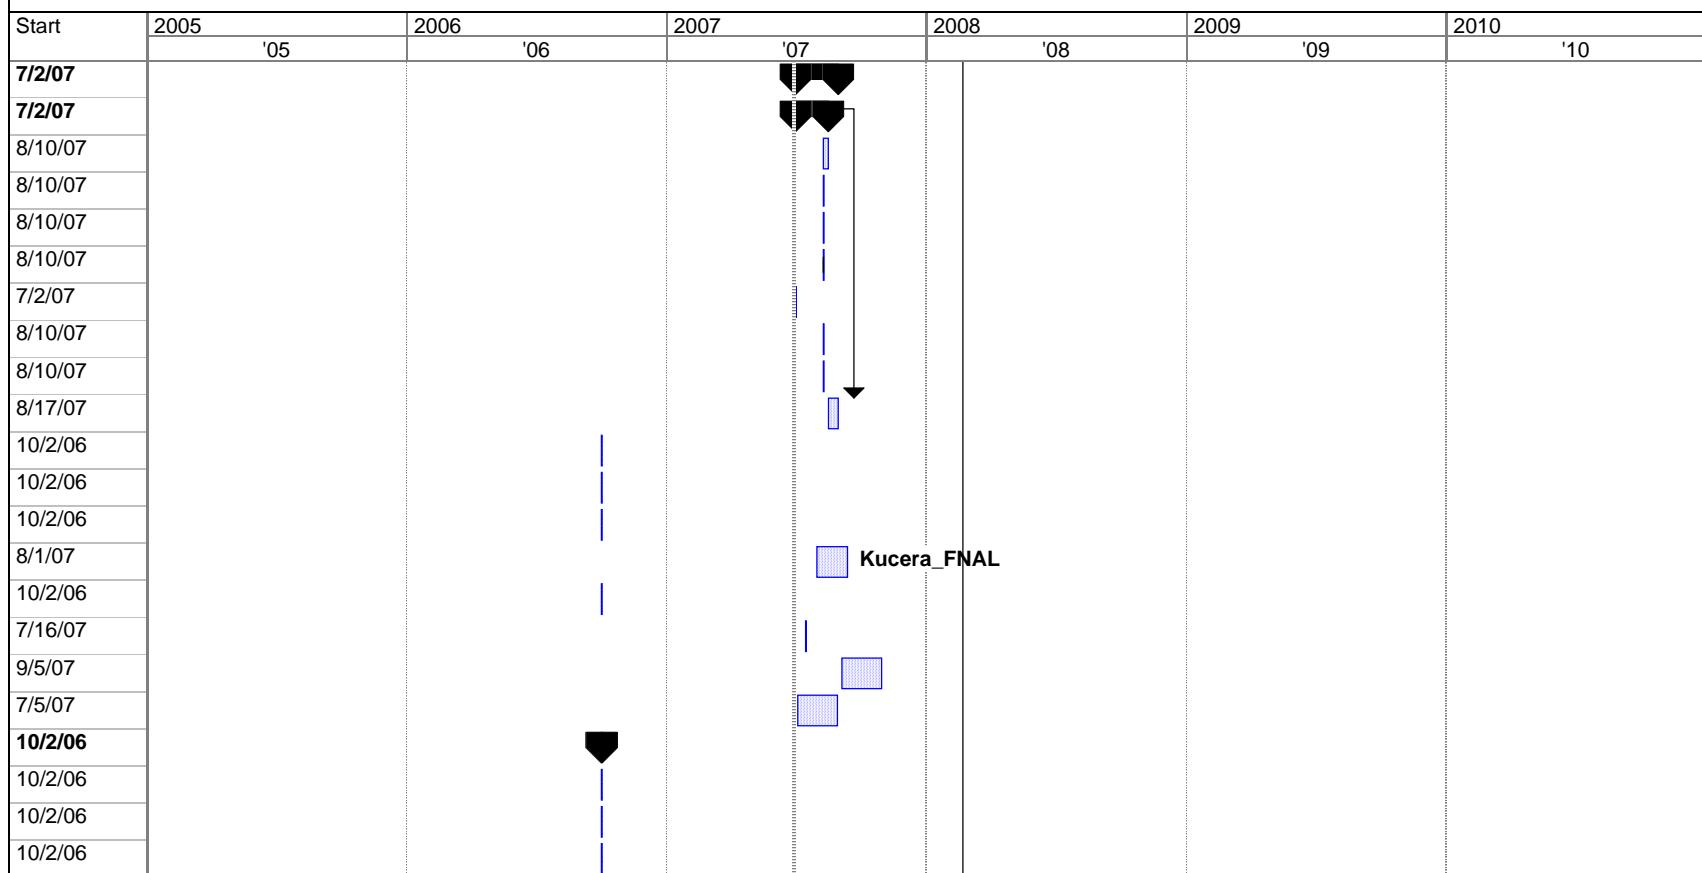


ILCTACControls_FNAL.mpp




ILCTACControls_FNAL.mpp




ILCTACControls_FNAL.mpp




ILCTACControls_FNAL.mpp




ILCTAControls_FNAL.mpp



ILCTACControls_FNAL.mpp




ILCTACControls_FNAL.mpp

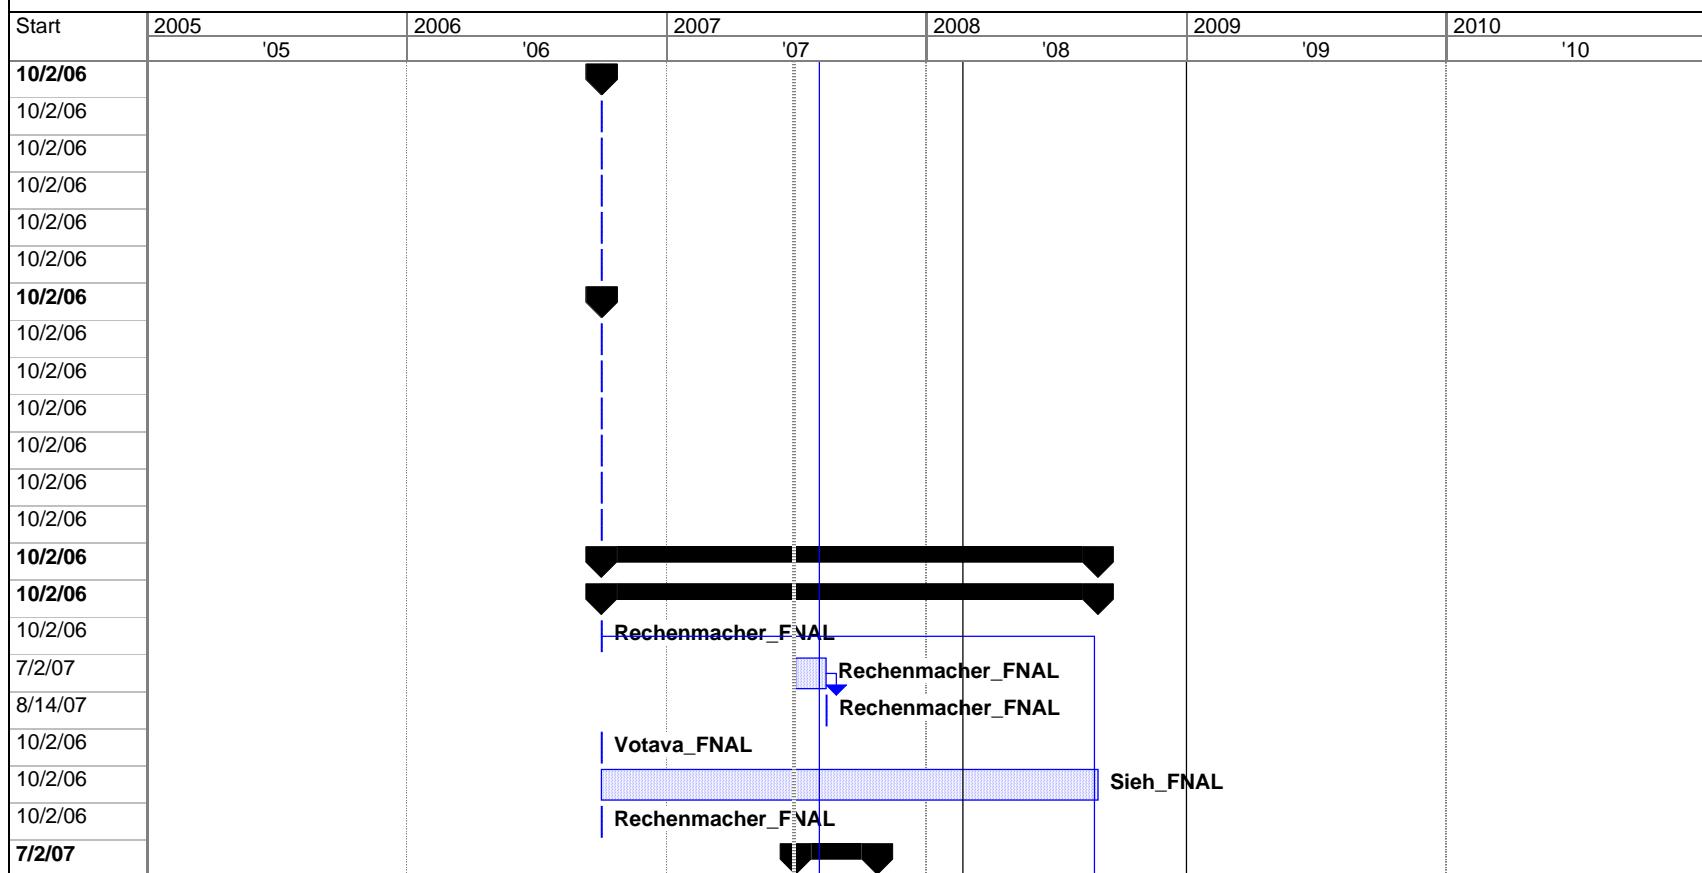

Project: ILCTAControls_FNAL.mpp Date: 6/28/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ILCTAControls_FNAL.mpp

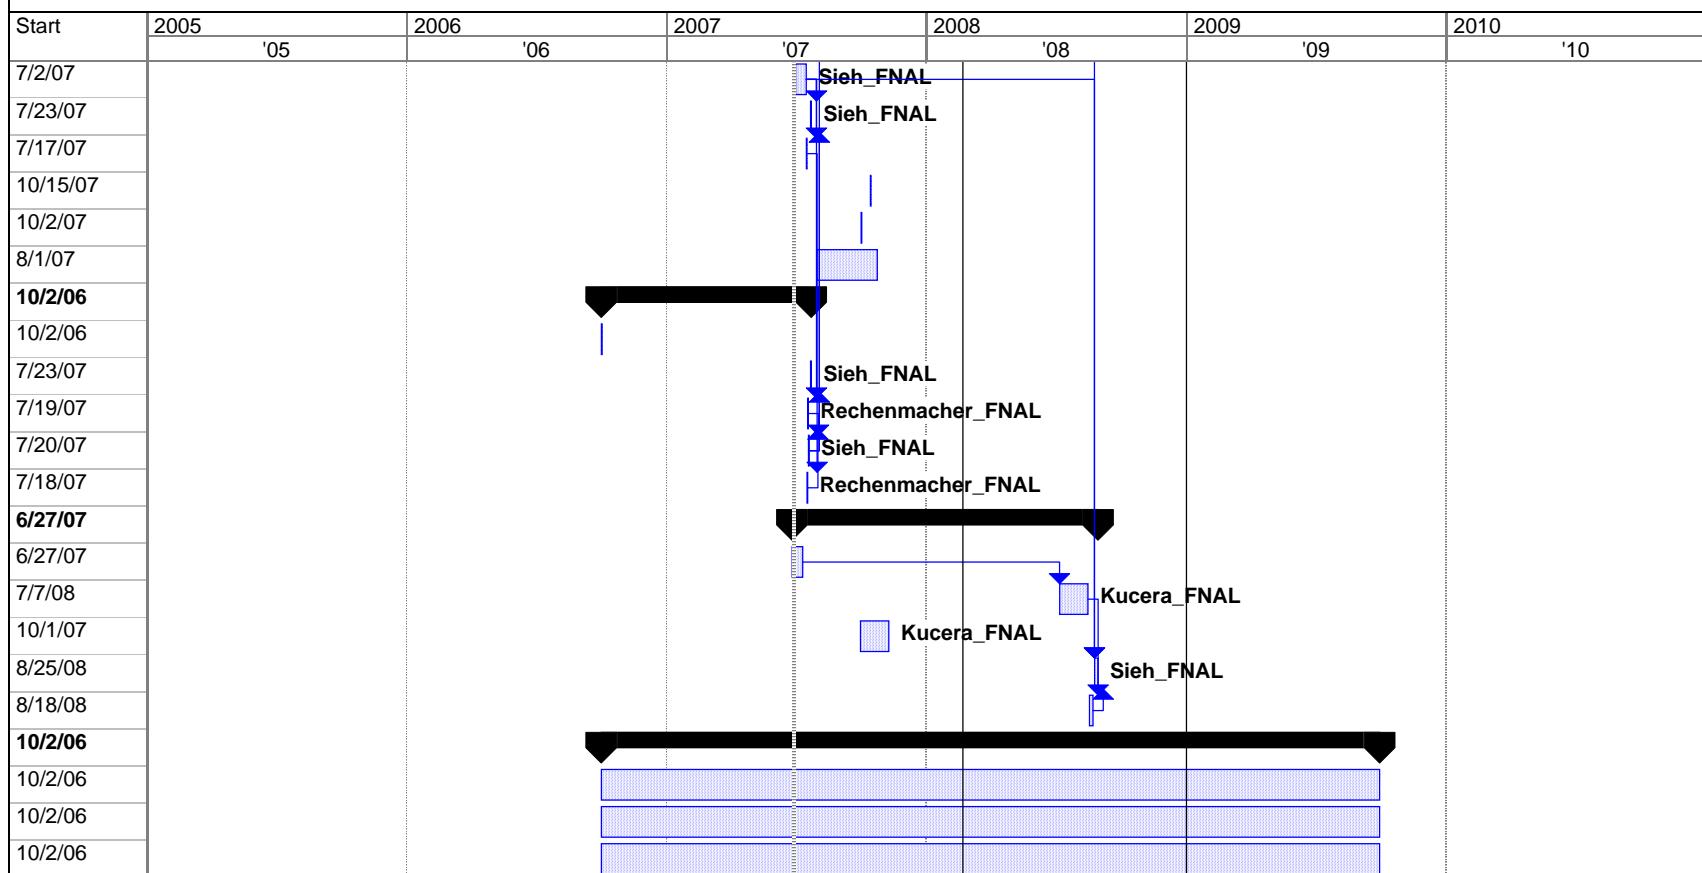

Project: ILCTAControls_FNAL.mpp
Date: 6/28/07

Task
Split
Progress



Milestone



Summary



Project Summary



External Tasks




External Milestone



Deadline




ILCTAControls_FNAL.mpp

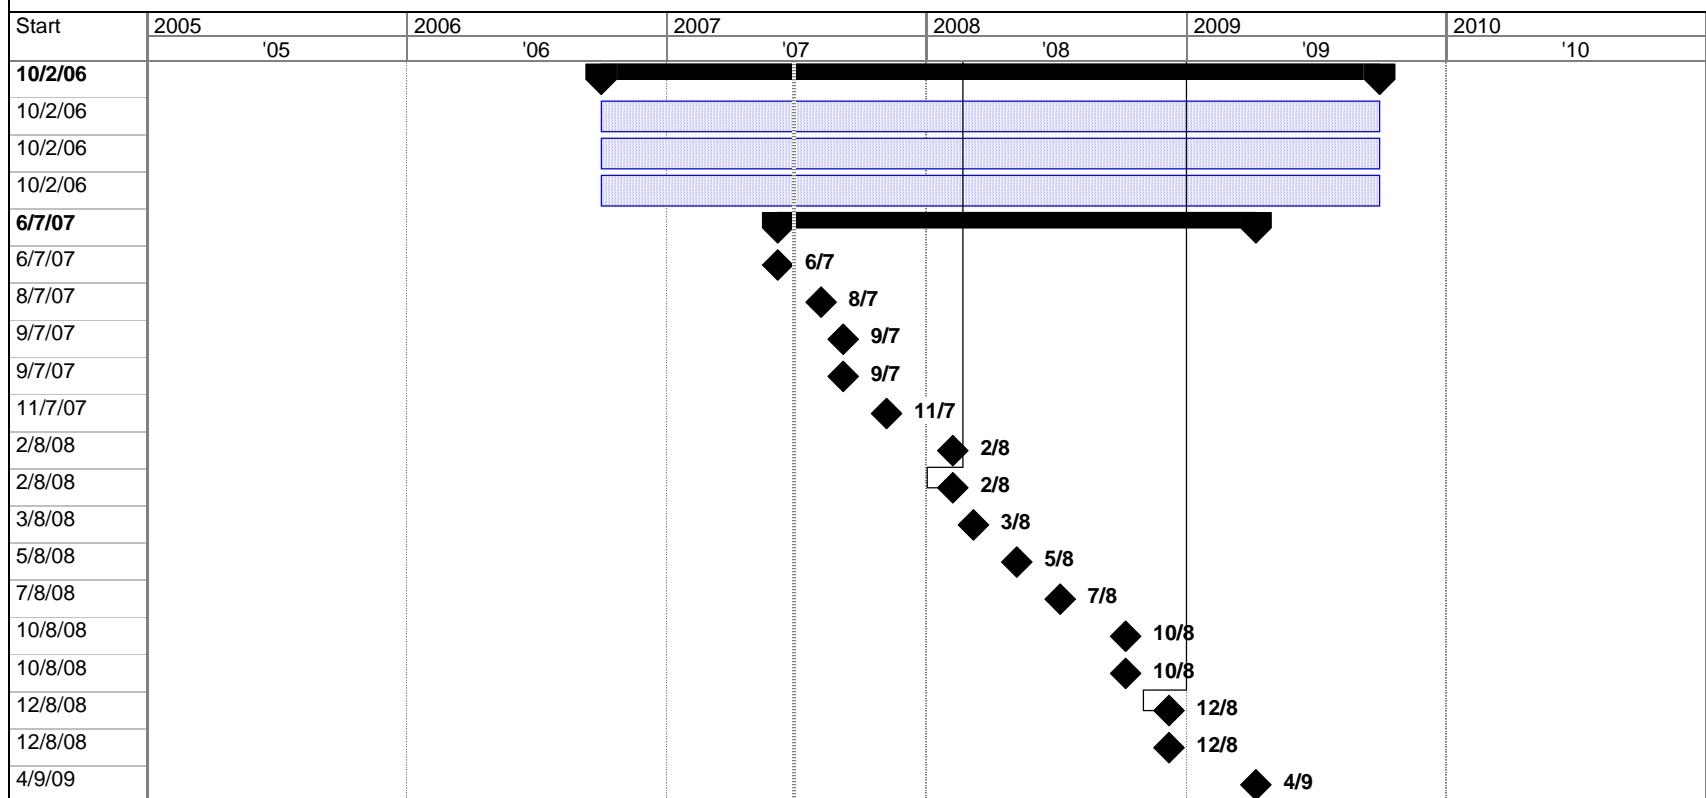

Project: ILCTAControls_FNAL.mpp
Date: 6/28/07

Task
Split
Progress



Milestone



External Tasks



Summary



External Milestone



Project Summary



Deadline

